

**PENGENDALIAN KONSTRUKSI PADA PAKET PERBAIKAN
JALAN RUAS TALANG BUNUT – LEMEUPIT PROVINSI
BENGKULU**

LAPORAN TEKNIK

*Sebagai Salah Satu Syarat untuk Menyelesaikan Program Profesi pada Program
Studi*

*Pendidikan Profesi Insinyur Sekolah Pascasarjana Universitas
Andalas*



MASYITA PURNAMA SARI, S.T.

NIM. 2541612079

PEMBIMBING:

Dr. Ir. Rina Yuliet, S.T., M.T., IPM

**PROGRAM STUDI PENDIDIKAN PROFESI
INSINYUR SEKOLAH PASCASARJANA
UNIVERSITAS ANDALAS**


PADANG

2026

ABSTRAK

Perbaikan Jalan Ruas Talang Bunut - Lemeupit merupakan kegiatan dari Presiden Republik Indonesia dalam rangka meningkatkan konektivitas jalan daerah. Sehingga Presiden mengeluarkan Instruksi Presiden dalam rangka perbaikan jalan daerah. Pembangunan ini memiliki pekerjaan timbunan pilihan, lapis fondasi agregat kelas A, laston lapis antara (AC-BC), laston lapis aus (AC-WC), pasangan batu mortar dan saluran drainase *U-Ditch*. Kegiatan ini dilaksanakan dalam waktu 164 hari kalender. Paket ini membutuhkan pengendalian agar paket kegiatan tersebut dapat berjalan optimal sehingga didapati pekerjaan yang memiliki tepat biaya, tepat mutu dan tepat waktu. Pada proses pengendalian ini mengatur seluruh kegiatan agar semua dapat berjalan sesuai dengan jadwal. Pengendalian paket ini juga termasuk pada kemandirian dan keselamatan dalam bekerja.

Kata Kunci : Timbunan pilihan, agregat kelas A, lapisan AC-BC, lapisan AC-WC, pasangan batu mortar

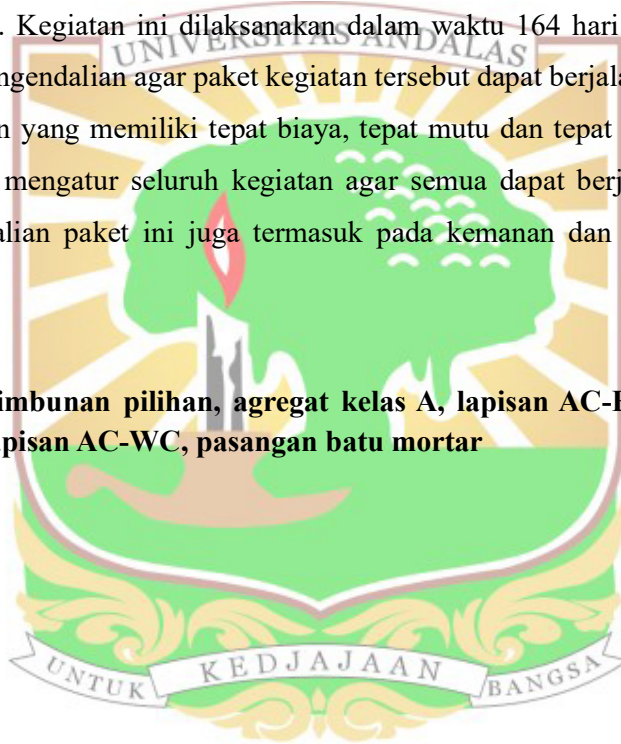

ABSTRACT

The Talang Bunut - Lameupit Road Repair is an activity of the President of the Republic of Indonesia in order to improve regional road connectivity. So the President issued a Presidential Instruction in order to repair regional roads. This development has selected embankment work, class A aggregate foundation layer, intermediate layer laston (AC-BC), wearing layer laston (AC-WC), mortar stone masonry and U-Ditch drainage channels. This activity is carried out within 164 calendar days. This package requires control so that the activity package can run optimally so that work is obtained that has the right cost, right quality and on time. In this control process, all activities are regulated so that everything can run according to schedule. Control of this package also includes safety and security at work.

Keywords: Selected fill material, class A agregate, AC-BC Layer, AC-WC Layer, stone masonry

